

Archaeological Survey – Field H1550

Pre-Construct Archaeology

Description of works:

In relation to the land located at Westmount Road, St Helier known as Field H 1550, the original request for access to the field was to carry out an archaeological survey of the geophysical landscape to determine any areas of historic significance that may require further archaeological investigation.

As part of the further investigation identified from our initial survey, ROKFCC JV plan to commission Pre-Construct Archaeology to undertake a programme of archaeological evaluation works. The proposed scope of works is to excavate ten 20m trenches, all measuring 1.8m wide and 0.5m deep to unearth possible archaeological features identified by a recent geophysical survey. The image in Fig. 01 displays the approximate location of the proposed trenches.

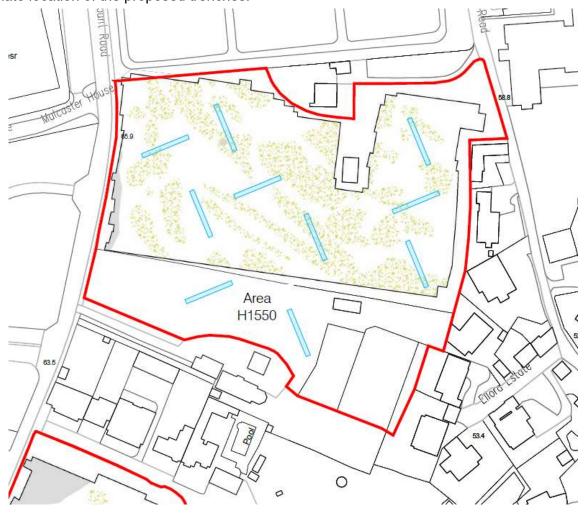


Fig. 01

Plant and Equipment:

The planned equipment of use will be a Volvo EW140 steel tracked excavator as shown in Fig. 02 below.



Fig. 02

A thorough dilapidation and time & date stamped photographic survey of the field and adjacent access will be conducted by ROKFCCJV before any works take place, this is to ensure that the ground and surrounding areas are re-instated back to the original condition.

The proposed survey working times are between 08:00AM and 17:00PM Monday to Friday commencing mid to end of October depending on access permission and availability of resources.

No works will be undertaken on Saturdays and Sundays

ROKFCC JV will continue to keep all parties and local neighbours informed throughout the process and do everything they can to minimise disruption.

Number of personnel:

There will be 3 nr. personnel attending.

Contact Details:

Name: Name: Company: ROKFCC JV Company: ROKFCC JV

Position: Project Manager Position: Design Construction Support

Telephone: Telephone:
